

Overview of the progress made in JA Chrodís

Work Package 1

6th EB Meeting
Treviso (Italy)
11th-12th of June, 2015



Teresa Chavarría
Catalina del Río
Patricia Cedié
Instituto de Salud Carlos III (ISCIII)

Work Package 1

Deliverables, Milestones & Activities

Achieved Deliverables


- The technical and financial interim report is a deliverable of the 1st year (month 12).
- Submission to Chafea is meant to be in the first two months of the second year.



☒ First Financial and Technical Interim Report Submission

Interim Technical Report Review Process: main comments from Chafea and improvements

- Simplification of the Structure and Contents.
- Deliverables and Milestones according to Grant Agreement.
- Improvement on the description of problems and how they were solved.
- Include the description of relevant meetings.
- Improvement of description on dissemination activities.
- Conclusions and recommendations for the 2nd year.

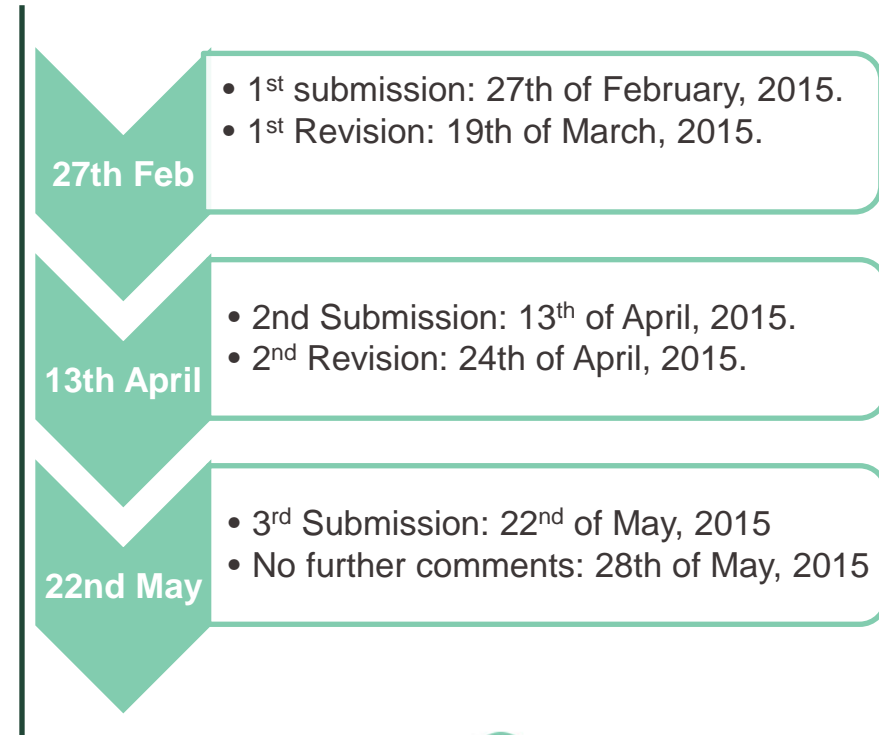

Deliverables to accomplish in the next 6 months (no delays foreseen)

	Jul	Aug	Sept	Oct	Nov	Dec
D08.1 2nd Interim Technical and Financial Report						
D08.2 Executive Board Minutes						
D 09. Annual report on Sustainability						

Achieved Milestones: January-June 2015

According to the Grant Agreement, the 1st Technical and Interim report is also a Milestone.





1st Technical and
Financial Interim Report
Submission.

Milestones to accomplish in the next 6 months (no delays foreseen)

	Jul	Aug	Sept	Oct	Nov	Dec
D08.1 2nd Interim Technical and Financial Report						

Achieved Activities / Tasks


- 
- ☒ EB Minutes
 - ☒ GB Meeting report and Work Plan (Ministry of Health)
 - ☒ General Assembly, 2nd Stakeholders Forum meeting reports
 - ☒ Advisory Board Meeting report

- 
- ☒ Communication with EIPonAHA and other European initiatives.
 - ☒ Follow up on WP activities
 - ☒ Organization of meetings
 - ☒ Amendment request

Amendment process review

Main changes requested

- FCIEN to FCSAI.
- New AP: AQuAS and APDP.
- WP 3 Leader: EHMA to AQuAS.
- Reallocation WP3 funds.
- Reduction of EPF's budget .
- Changes in deliverables (2, 3, 7, 9).
- Changes in staff from some of the Partners.
- New distribution of person days.

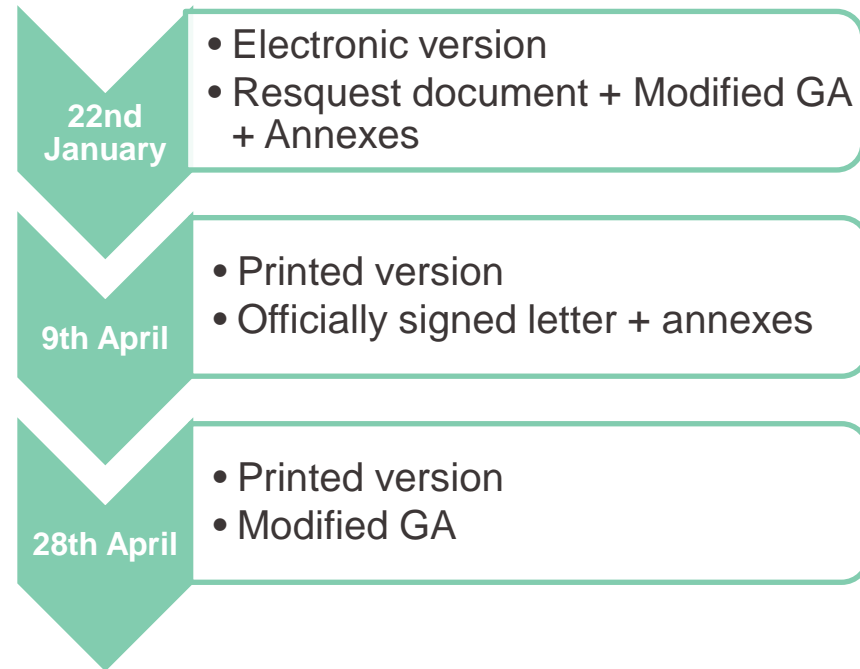

Amendment – Changes in Deliverables

- **Deliverable #2: Clearinghouse**
 - From M24 to M37
- **Deliverable #3: Online Help Desk**
 - From M30 to M37
- **Deliverable #7: Reports Multimorbidity**
 - The report on beneficial interventions will include a review of existing care pathways, thus moving report delivery from M18 to M24.
- **Deliverable #9: Annual Reports on Sustainability**
 - From M36 to M15, M27, M37

Activities/Tasks to accomplish in the next 6 months


	Jul	Aug	Sept	Oct	Nov	Dec
1. Advisory Board Work Plan proposal						
2. WP1 Indicators						
3. Semester Progress Report						
4. Semester Financial Report						

Activities/Tasks to accomplish in the next 6 months


	Jul	Aug	Sept	Oct	Nov	Dec
5. Organization of relevant JA meetings (EB, AB, GB)						
6. Dissemination Activities						
7. Follow up on WP activities						

Collaboration with other WPs / Initiatives

Collaboration with other WPs and/or initiatives



Collaboration with other WPs and/or initiatives



Dissemination Activities

Scientific and policy level

Dissemination Activities

Scientific Level

- XX AMD Congress (13th of May, Genoa (Italy)).


Policy Level

- International University Menendez Pelayo, 3rd of July. Confirmed.
- JA-CHRODIS participation in Gastein. (to be confirmed).
- JA-CHRODIS high level meeting Parliament level (to be defined).


Financial Overview of the JA-CHRODIS

Financial Overview 2014

Expenses Jan-June 2014 vs. Total budget per WP

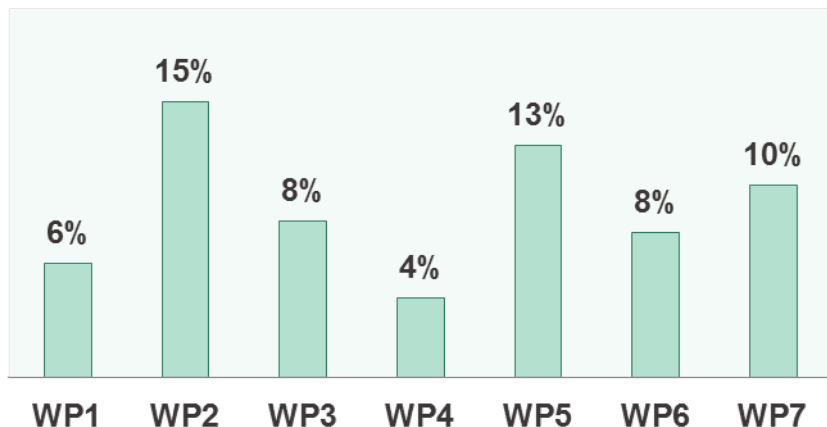


Expenses 2014 vs. Total budget per WP

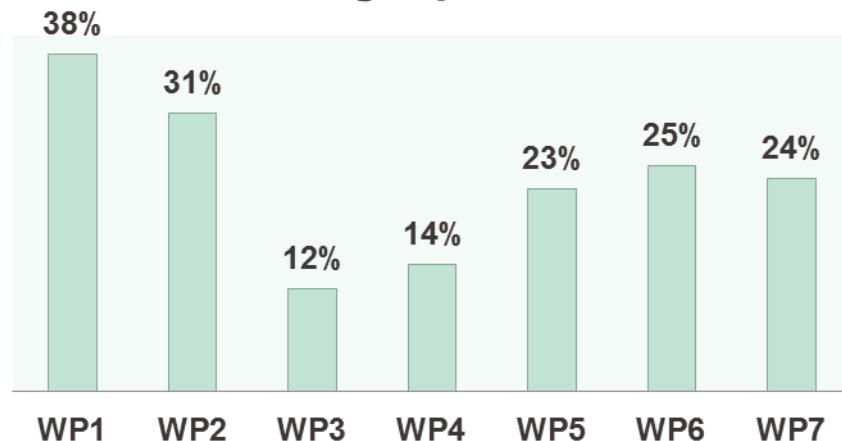


- **Budget JA CHRODIS: 9,307,927**
- **Budget consumed 2014: 23%**

Financial Overview 2014 – Person Days

**Distribution of Person Days
2014-2017**

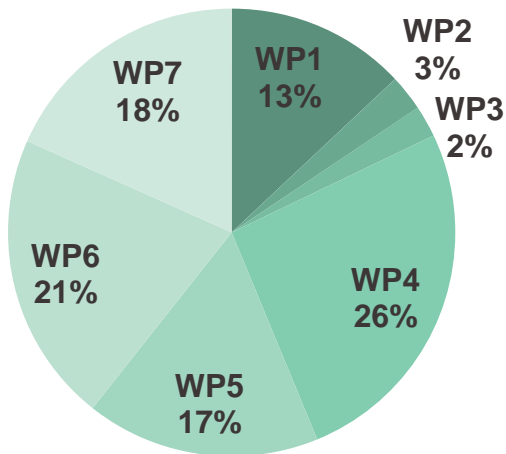

**P/D consumed 2014 vs. Total per WP
(11/03/15)**

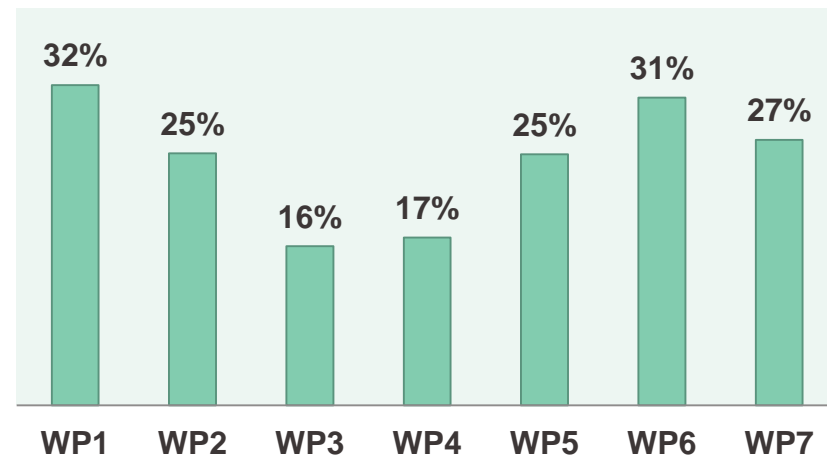

- **Person Days JA CHRODIS: 32,558**
- **P/D consumed 2014: 25%**

Lesson learnt and Recommendations

Period January-June 2015

Room for Coordination WP Improvement

- More proactive communication with WPL's.
- Foster synergies among WP and with other initiatives and contribute to create a common vision of the JA.
- Development of new collaborations and establishment of contacts at the international level.
- Promote visibility at the policy level: set up Meetings with Parliamentarians, presentation of JA results in European Health Policy events, Development of policy briefings etc.

Room for Coordination WP Improvement

- Improve communication with our Governing Board and Advisory Board.
- Create a community network for the sustainability of the JA-Chrodis' outcomes.
- Improve timeframes of management activities: minutes approval, new collaborating partners involvement, etc.
- Improve organization and structure of meetings.

THANK YOU!

The Joint Action on Chronic Diseases and Promoting Healthy Ageing across the Life Cycle (JA-CHRODIS)*



Co-funded by
the Health Programme
of the European Union

* This presentation arises from the Joint Action addressing chronic diseases and healthy ageing across the life cycle (JA-CHRODIS), which has received funding from the European Union, under the framework of the Health Programme (2008-2013).

Overview of the progress made in JA Chrodis

Work Package 2 – Communication




Presenter
EuroHealthNet

Work Package 2

Deliverables, Milestones & Activities

Achieved Deliverables and Milestones

- All deliverables & milestones: due in year 1
- Year 2 has been about applying and refining the comms tools available.

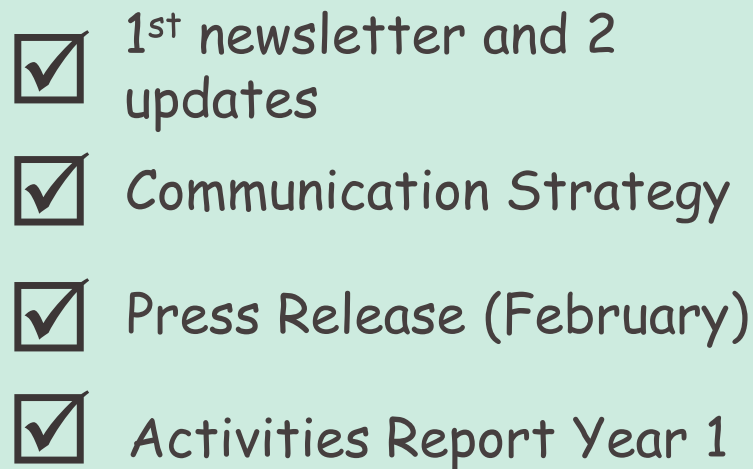- 
- ☒ 1st newsletter and 2 updates
 - ☒ Communication Strategy
 - ☒ Press Release (February)
 - ☒ Activities Report Year 1

Activities of the past 6 months

	Jan	Feb	Mar	Apr	May	Jun
Partners Reporting				Report		
Newsletter/ Updates/PR		Newsletter		Update		Update
		Press Rel.				
Comms Plan Work 2015			Approved			
Spelling Doc/ Style Guide				Approved		
Authorship Guidelines					Received	Approval pending
Partners' websites						Requested

Activities in the next/past 6 months


	Jul	Aug	Sept	Oct	Nov	Dec
Act. / Task #	Title		Shows delay if applicable			
Act. / Task #		Title		Shows delay if applicable		
Act. / Task #		Title			Shows delay if applicable	
Act. / Task #		Title			Shows delay if applicable	
Act. / Task #			Title		Shows delay	
Act. / Task #			Title		Shows delay	

Activities to accomplish in the next 6 months

	Jul	Aug	Sept	Oct	Nov	Dec
Newsletter and Updates	Update				Newsletter	
			Update	Update		Update
Dissemination at political level	Draft Strategy					
Partners' websites						
Video						
Translation	Brochures					
Ongoing	Website, Social Media, Database					

Collaboration with other WPs / Initiatives

Collaboration with other WPs and/or initiatives



Dissemination Activities

Scientific and policy level

Dissemination Activities



Scientific Level

- Insert your activity
- Insert your activity
- Insert your activity
- Insert your activity



Policy Level

- Insert your activity
- Insert your activity
- Insert your activity
- Insert your activity

The Joint Action on Chronic Diseases and Promoting Healthy Ageing across the Life Cycle (JA-CHRODIS)*



Co-funded by
the Health Programme
of the European Union

* This presentation arises from the Joint Action addressing chronic diseases and healthy ageing across the life cycle (JA-CHRODIS), which has received funding from the European Union, under the framework of the Health Programme (2008-2013).

Overview of the progress made in JA Chrodis

Work Package 3 - Evaluation



Rogério Ribeiro
APDP – Diabetes Portugal


Carme Carrion, Noemí Robles, Mireia Espallargues
AQuAS, Spain
Maria Pilar Acuña, Asensio Santiago
FFIS, Spain

Work Package 3

Deliverables, Milestones & Activities

WP3 Achieved Milestones

General Aim: To monitor JA-CHRODIS through Evaluation Indicators.

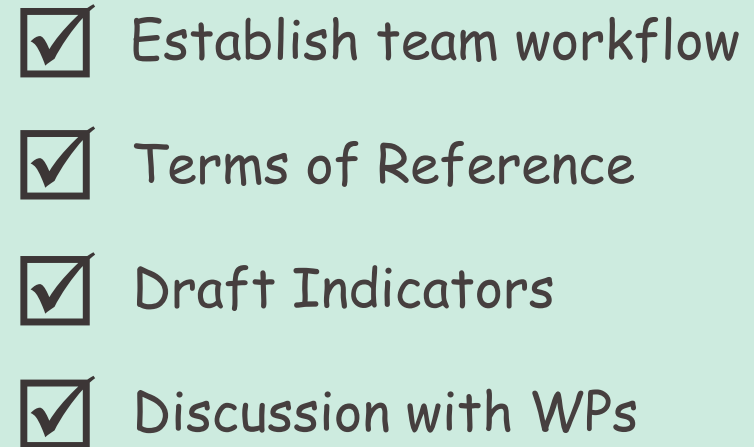- 
- ☒ Establish team workflow
 - ☒ Terms of Reference
 - ☒ Draft Indicators
 - ☒ Discussion with WPs

Milestones to accomplish in the next 6 months

	Jul	Aug	Sept	Oct	Nov	Dec
Milestone 1	Agreed Indicators					
Milestone 3			Interim Evaluation Report			

Achieved Deliverables

Extended Aim: To prepare JA-CHRODIS impact evaluation framework.


- ☒ Draft Evaluation Plan
- ☒ Commission to develop Impact Assessment Plan

Deliverables to accomplish in the next 6 months

	Jul	Aug	Sept	Oct	Nov	Dec
Deliverable 1	Evaluation Plan					
Deliverable 2	Impact Plan					
Deliverable 3					Interim report	

Achieved Activities / Tasks

Time has been regained and new goals are being proposed.


- 
- ☒ Event Survey Analysis
 - ☒ Alignment of Evaluation
 - ☒ Partners satisfaction
 - ☒ Impact beyond Project

Activities/Tasks to accomplish in the next 6 months

	Jul	Aug	Sept	Oct	Nov	Dec
Task #1	Evaluation Plan					
Task #2			Data Collection			
Task #3				Midterm Evaluation Report		
Task #4	Impact Plan					
Task#5			Congress			

Collaboration with other WPs / Initiatives

Collaboration with other WPs and/or initiatives

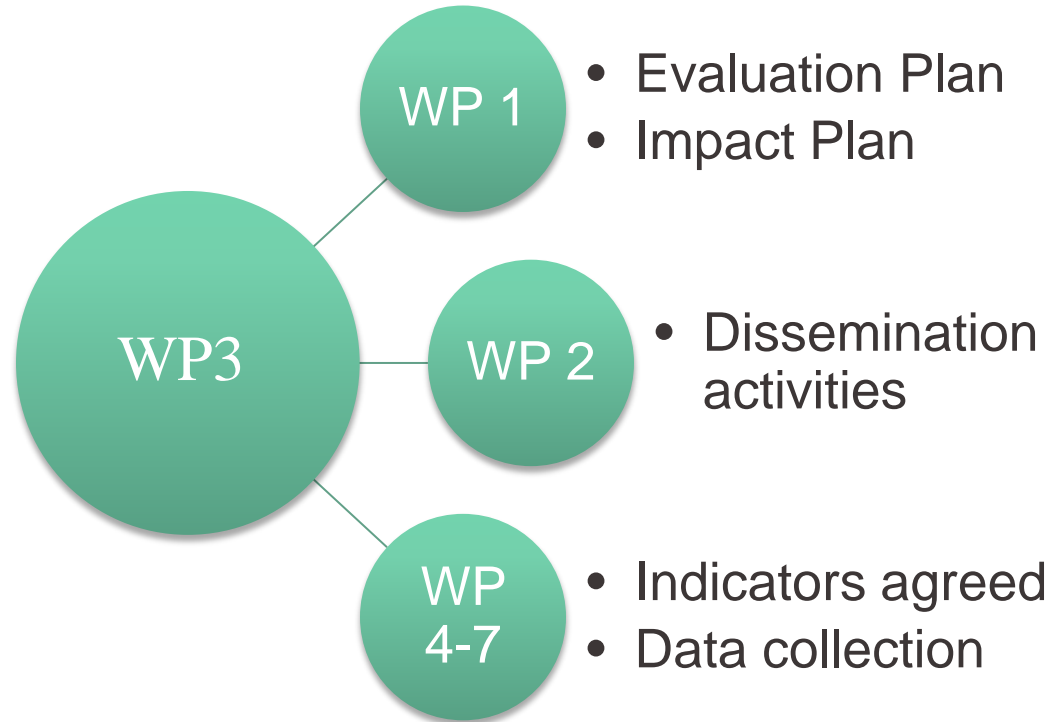

Dissemination Activities

Scientific and policy level

Dissemination Activities



Scientific Level

- Iberoamerican Congress of Epidemiology and Public Health (Sept. 2015)



Policy Level

- Debate at Portuguese Diabetes Congress (Feb. 2016)

The Joint Action on Chronic Diseases and Promoting Healthy Ageing across the Life Cycle (JA-CHRODIS)*



Co-funded by
the Health Programme
of the European Union

* This presentation arises from the Joint Action addressing chronic diseases and healthy ageing across the life cycle (JA-CHRODIS), which has received funding from the European Union, under the framework of the Health Programme (2008-2013).

Overview of the progress made in JA Chrodis

Work Package 4



Enrique Bernal Delgado
IACS

Work Package 4

Deliverables, Milestones & Activities


Planned activities 2015 - timeline

Activities / Deliverables / Milestones	2015 Months and Milestones Dates (M)											
	Ene	Feb	Mar	Abr	May	Jun	Jul	Ago	Sep	Oct	Nov	Dic
Development of assessment criteria (Task 1)												
Development of assessment criteria (Delphi on Health Prevention & Promotion cont.)												
Development of assessment criteria (Delphi on organizational interventions (with particular emphasis in interventions on multi morbid patients)												
Development of assessment criteria (Delphi on patient empowerment interventions))												
Development of assessment criteria (Delphi on Diabetes as a case-study)												
Definition of assessment criteria (M4.1)						D1					D2	D3
Design of a set of on-line tools aimed at providing users with guidance on development, implementation and evaluation of Chronic Care (CC) practices (Task 2)												
Assessment tool piloting including usability and accesibility testing (no storage)												
Other on-line tools available for PKE												
Online toolkit (M4.2)												
Technological platform and services to support post-JA activities (Task 6)												
Content management development												
User management development												
Assessment tool piloting (with storage)												
Setting an on-line front-desk with expert consultants available to help users in the actual development, implementation and evaluation of CC practices (Task 3)												
Help-desk services ready for piloting (M4.3)												
End users' surveys (inlcluding policy-makers, healthcare professionals, patients's perspective)												
Creation of a repository of excellent CC practices and Policies across Europe (Task 4)												
Development of a digital library where best knowledge on CC is made available for interested audiences (Task 5)												
End users' surveys (inlcluding policy-makers, healthcare professionals, patients's perspective)												
Clearinghouse and Digital Library ready for piloting (M4.4)												
PKE ready for service (M4.5)												
Coordination with EIP-AHA (activity not foreseen in the grant agreement)												
Business plan (activity not foreseen in the grant agreement)												

Achieved Activities / DELPHI 1

15	J	F	M	A	M	J
D1					X	


Delphi on Health Prevention
& Promotion

- 
- ☒ DELPHI 1 consultation
 - ☒ Face to Face meeting
 - ☒ List of criteria and specific weights
 - ☒ final report D1

Achieved Activities / DELPHI 2

15	J	A	S	O	N	D
D2					X	

Delphi on organizational
interventions
(with particular emphasis in
interventions on multi morbid
patients)

- 
- ☒ Literature review
 - ☒ Questionnaire
 - ☒ Experts recruitment
 - ☒ Launching 1st Consultation

Achieved Activities / DELPHI 3

15	J	A	S	O	N	D
D3						X

DELPHI on Patient Empowerment
interventions

- ☒ Literature review
- ☒ Starting identification of experts

PKE/Tasks accomplished in the last 6 months

	Jan	Feb	Mar	Apr	May	Jun
MeSH		X	MeSH automated labelling through NLM API			
Metadata	Metadata user profiles designed				X	
Interface	CH and DL search results screen designed				X	
Convergence with EIP AHA	CHRODIS proposal for convergence in DL				X	

PKE/Tasks to be accomplished in the next 6 months


	Jul	Aug	Sept	Oct	Nov	Dec
Metadata design		X	Clearinghouse content data model			
Programming		X	Programming PKE user search interface			
Submission Form			X	Practice submission form D1		
Evaluation Form			X	Practice assessment application D1		
Piloting		Clearinghouse piloting D1 (no storage)				X

PKE/Tasks to be accomplished in the next 6 months (2)


	Jul	Aug	Sept	Oct	Nov	Dec
Biz Model			X	WP4 Business Model Drafted		
EIP AHA	X	Convergences in DL introduced				
DL		Browsing contents for digital library				X
Helpdesk			X	Help Desk Integration		

Collaboration with other WPs / Initiatives

Collaboration with other WPs and/or initiatives

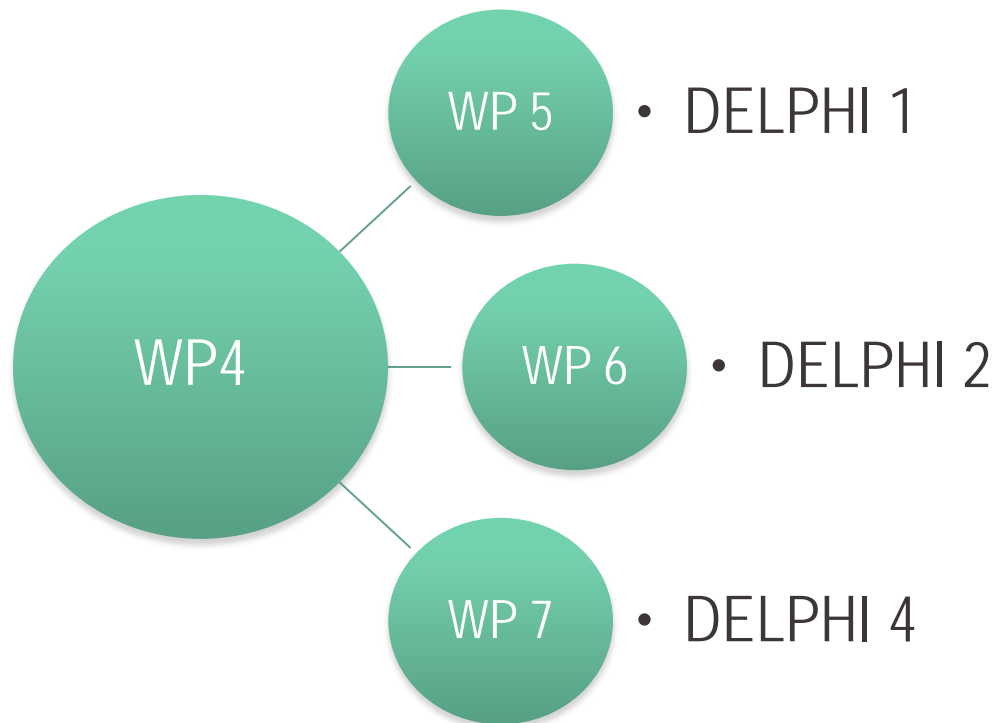

Collaboration with other WPs and/or initiatives



Dissemination Activities

Scientific and policy level

Dissemination Activities

Scientific Level

- **Geriatrics Annual Conference in Aragon. CHRODIS-JA:** addressing chronic diseases and promoting healthy ageing across the life cycle ; Zaragoza España (19th March 2015)
- **4 Papers** from Delphi envisaged - under discussion

Policy Level

- Chronic Diseases and Healthy Ageing Workshop ; The Hague/The Netherlands** (12th and 13th February 2015)
- **European Summit on Innovation for Active and Healthy Ageing;** Brussels/ Belgium (10th of March 2015)

The Joint Action on Chronic Diseases and Promoting Healthy Ageing across the Life Cycle (JA-CHRODIS)*



Co-funded by
the Health Programme
of the European Union

* This presentation arises from the Joint Action addressing chronic diseases and healthy ageing across the life cycle (JA-CHRODIS), which has received funding from the European Union, under the framework of the Health Programme (2008-2013).

Overview of the progress made in JA Chrodis

Work Package 5

Health Promotion and Primary
Prevention



Presenter
Institution

Work Package 5

Deliverables, Milestones & Activities

Activities since February 2015

- ✓ Developed summary of country reports (EuroHealthNet)
- ✓ Developed first version of questionnaire for the documentation of Good Practices
- ✓ April 23rd/24th attendance at Delphi F2F Meeting organized by WP 4
- ✓ Developed extended version of questionnaire for the documentation of Good Practices including Delphi Criteria

Activities since February 2015 (II)

Work Package Meeting on May 26th 2015 in Cologne


- 21 Participants
- Key topics:
 - Conceptual discussion on the documentation of GP examples (Task 3)
 - Draft concept for health promotion conference in Vilnius, Lithuania (Task 4)
 - Perspectives in 2016 (Task 5)

Deliverables to accomplish in the next 6 months

	Jul	Aug	Sept	Oct	Nov	Dec
Report GP examples	Report GP Examples					
Conference						

Collaboration with other WPs / Initiatives

Collaboration with other WPs and/or initiatives



- Political dissemination of the conference
- Collaboration in conference PR
- Continuous collaboration in conducting the evaluation of WP 5 and the JA as a whole
- Coordination on the GP documentation interface of the PKE

Dissemination Activities

Scientific and policy level

Dissemination Activities



Scientific Level

- Presentation of the Joint Action in cooperation with Caroline Costongs (EuroHealthNet) at "Poverty and Health", March 2015 in Berlin

The Joint Action on Chronic Diseases and Promoting Healthy Ageing across the Life Cycle (JA-CHRODIS)*



Co-funded by
the Health Programme
of the European Union

* This presentation arises from the Joint Action addressing chronic diseases and healthy ageing across the life cycle (JA-CHRODIS), which has received funding from the European Union, under the framework of the Health Programme (2008-2013).

Overview of the progress made in JA Chrodis

Work Package 6

Multimorbidity



Rokas Navickas / Elena Jurevičienė
VULSK

Graziano Onder / Federica Mammarella
AIFA

Work Package 6

Deliverables, Milestones & Activities

Task 3. overview

- List of criteria:
 - Cost effectiveness
 - Applicability
 - Replicability
- Identify target population for each component based on risk factors
- Define minimum set of key characteristics to standardize them

Achieved Deliverables

Analysis of large
administrative
databases(M12)




6 publications on
EJIM

Deliverables to accomplish in the next 6 months

	Jul	Aug	Sept	Oct	Nov	Dec
Deliverable 6.1	Reports and common guidelines for care pathways for MM patients					

Achieved Milestones

Milestone:
Analysis of large
administrative
databases

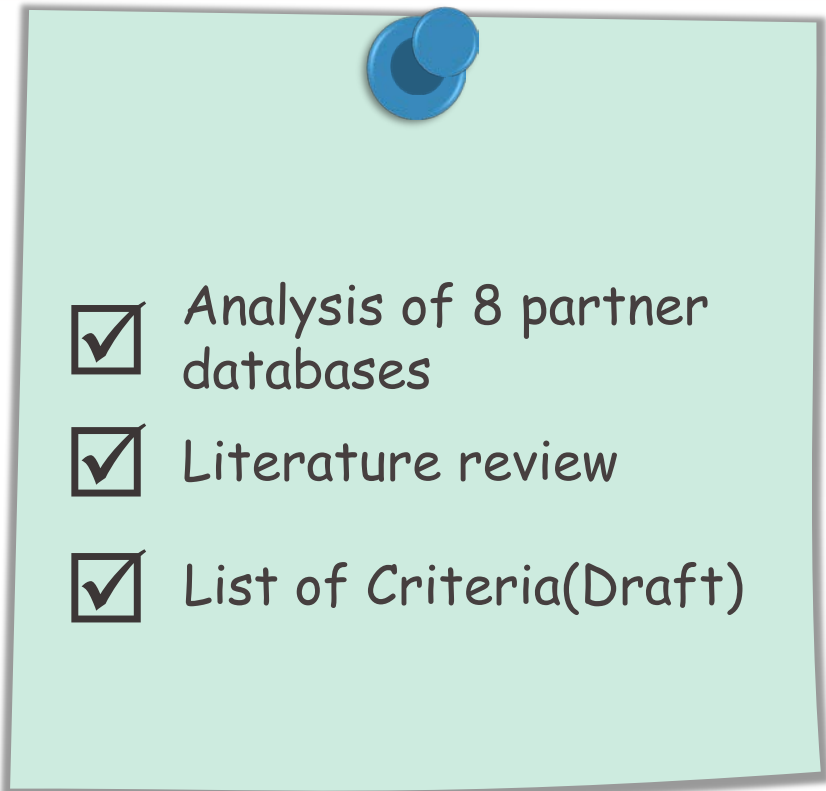
- 
- ☒ Analysis of 8 partner databases
 - ☒ Literature review
 - ☒ List of Criteria(Draft)

Milestones to accomplish in the next 6 months

	Jul	Aug	Sept	Oct	Nov	Dec
Milestone 1			Delphi process			
Milestone 2			Info pack for expert meeting			
Milestone 3				Expert meeting		
Milestone 4					Joint Wp6&Wp7 publication	

Achieved Activities / Tasks

**Assess and select good practices
on management of multi-morbid
patients**

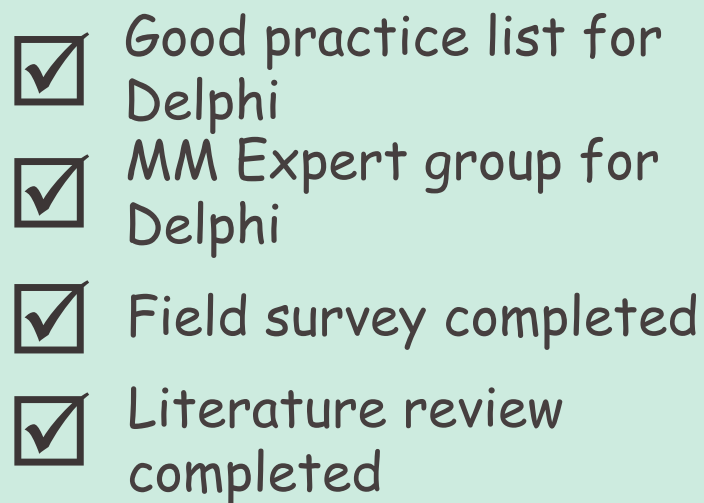
- 
- ☒ Good practice list for Delphi
 - ☒ MM Expert group for Delphi
 - ☒ Field survey completed
 - ☒ Literature review completed

Activities/Tasks to accomplish in the next 6 months

	Jul	Aug	Sept	Oct	Nov	Dec
Act. / Subtask 1	Select experts for “clinical” meeting					
Act. / Subtask 2	Report on applicability and replicability of criteria					
Act. / Subtask 3	Finalize results on cost effectiveness analysis					
Act. / Subtask 4	Identify target population					
Act. / Subtask 5	Key characteristics to standardize criteria					
Act. / Subtask 6			Organize expert meeting			

Collaboration with other WPs / Initiatives

Collaboration with other WPs and/or initiatives



Dissemination Activities

Scientific and policy level

Dissemination Activities

Scientific Level

- 6 EJIM publications
- LANCET letter to editorial
- Baltic Family Medicine Conference 2015
- Extended database analysis

Policy Level

- Baltic Family Medicine Conference 2015 (March 2015)
- 18th European Health Forum Gastein (Oct 2015)
- Multimorbidity Conference (Oct 2015)

The Joint Action on Chronic Diseases and Promoting Healthy Ageing across the Life Cycle (JA-CHRODIS)*



Co-funded by
the Health Programme
of the European Union

* This presentation arises from the Joint Action addressing chronic diseases and healthy ageing across the life cycle (JA-CHRODIS), which has received funding from the European Union, under the framework of the Health Programme (2008-2013).

Overview of the progress made in JA Chrodis

Work Package 7



Angela Giusti, Marina Maggini
National Institute of Health, Italy

Jelka Zaletel, Milivoj Piletic
National Institute of Public Health, Slovenia

Work Package 7

Deliverables, Milestones & Activities

Milestones to accomplish in the next 6 months

	Jul	Aug	Sept	Oct
Milestone 1 Expert overview on successful strategies to improve prevention of diabetes, and the quality of care for people with diabetes (M18)				
Milestone 2+3 Workshop to analyze collected data on processes in NDP development, implementation, sustainability (M22) joined with Expert/policy maker meeting (M20)				

Achieved Activities / Tasks

T1-T4: Questionnaire on practices for prevention and management of diabetes

First phase

provision of a structured overview about current programs (interventions, initiatives, approaches or equivalents)

Second phase *(ongoing)*

analysis of programs/interventions/strategies/experiences reported by partners during the first phase (potential good practices)


Achieved Activities / Tasks

Task 1 – Prevention of diabetes:
focus on people at high risk

Task 2 – Secondary prevention of
Type 2 Diabetes

Task 3 – Health promotion
interventions

Task 4 – Education strategies and
approaches/training for
professionals

- 
- ✓ Data collection (*first phase*)
 - ✓ Analysis of data
 - ✓ Data quality check
 - ✓ Drafting report
 - ✓ Definition of criteria for practices
 - ✓ Data collection (*second phase, ongoing*)

T1- T4: Questionnaire collected

Austria
Belgium
Finland
France
Germany
Greece
Ireland
Italy
Lithuania
Norway
Portugal
Slovenia
Spain
United Kingdom
Czech Republic
Denmark
Malta

WP7 partners

Other
CHRODIS
partners


Other EU MSs

Hungary (EPF int.)
Romania (Advisory Board)


Croatia
Cyprus
Netherlands

T1-T4: Reported practices/programs

Programs on prevention of diabetes
(n=35)



Programs on management of diabetes
(n=28)



T1-T4: Reported practices/programs

Programs on patient education
(n=26)



Programs on training for professionals
(n=29)



Achieved Activities / Tasks

T5: Questionnaire on National Diabetes Plans

First phase


Completed questionnaires with follow up TCs with most of respondents
Draft report with data approved from respondents

Second phase *(ongoing)*

Agreement with EU Observatory on Health Systems and Policies to produce Policy Brief
Additional data collection with draft report used as a background document

Achieved Activities / Tasks

Task 5 – National Diabetes Plans

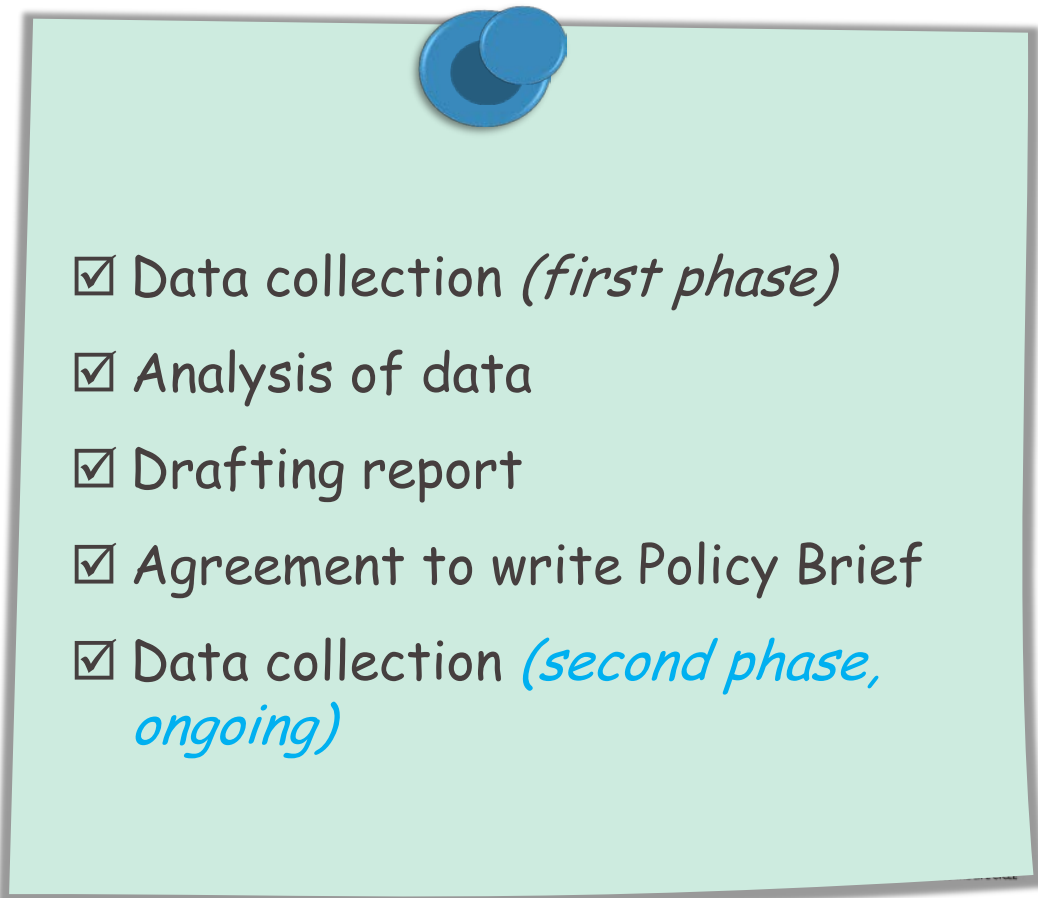- 
- ✓ Data collection (*first phase*)
 - ✓ Analysis of data
 - ✓ Drafting report
 - ✓ Agreement to write Policy Brief
 - ✓ Data collection (*second phase, ongoing*)

Collaboration with other WPs / Initiatives

Collaboration with other WPs and/or initiatives

WP7

WP 6

- Lithuania – Co-Leader WP6 (WP7 AP) → Study on Influence of Diabetes on Health Care Resources Usage in Multimorbid Patients

EMPATHiE

- Co-coordinator David Somekh (WP7 CP) → Collate and review results relevant to diabetes
- WP leader Valentina Strammiello (WP7 AP)

EIP-AHA

- Greece (WP7 AP) – Group 3 Integrated care → EIP on AHA B3 Action Group: Maturity Model for the assessment of Integrated care services

Dissemination Activities

Scientific and policy level

Dissemination Activities



Scientific Level

Scientific publication on
Annals of ISS (open
access)

AMD National Congress



Policy Level

Policy Brief on National
Diabetes Plans

Workshop on «how-to-do-
policy-speak»

Involvement of Governing
Board? TBD



Igea: da progetto a sistema

- il progetto
- il sistema
- documenti Igea
- convegni
- formazione

Sul territorio

- sistema Igea
- progetto Igea

Strumenti per gli operatori

- documenti
- tools
- link

Diabete

- cos'è il diabete
- fatti e numeri
- farmaci e diabete
- disuguaglianze e diabete

Chi siamo

- contattaci

[home](#) > CHRODIS-JA: la Joint Action europea sulle malattie croniche...

Integrazione, gestione e assistenza

JA-CHRODIS: la Joint Action europea sulle malattie croniche

La "European Joint Action on Chronic Diseases and Promoting Healthy Ageing across the Life Cycle" (CHRODIS-JA) è una azione congiunta europea dedicata alle malattie croniche e alla promozione dell'invecchiamento "in salute" nel corso della vita. CHRODIS-JA mira infatti a promuovere lo scambio di buone pratiche tra Paesi europei e rientra nel programma europeo "Health programme 2008-2013".



Ultime notizie dalla JA

4/6/2015 - Empowerment dei pazienti: un convegno a Bruxelles
Sono disponibili sul sito dell'European Patient Forum (EPF) i materiali del convegno "Empowered patients are an asset to society", organizzato il 20-21 maggio 2015 a Bruxelles. L'evento è stato dedicato interamente all'empowerment dei pazienti, argomento fondamentale per coloro che si occupano di malattie croniche. Per maggiori informazioni sul convegno e per scaricare le presentazioni visita la [pagina dedicata sul sito dell'EPF](#).

Lo scenario

Entro il 2060 si prevede che il numero di europei con età superiore a 65 anni aumenti da 88 a 152 milioni, con una popolazione anziana doppia di quella dei bambini sotto i 15 anni. Le malattie croniche (come lo scompenso cardiaco, l'insufficienza respiratoria, i disturbi del sonno, il diabete, l'obesità, la depressione, la demenza, l'ipertensione), colpiscono l'80% delle persone oltre i 65 anni e spesso si verificano contemporaneamente. La co-morbidità è associata a un declino di molti aspetti della salute, come la qualità della vita, la mobilità, la capacità funzionale, con un conseguente aumento di stress psicologico, ospedalizzazioni, uso delle risorse sanitarie e mortalità.

Obiettivi e
L'obiettivo è trasferire le conoscenze sulle malattie croniche, e sulla salute determinata

General reflection on methods of dissemination of WP7 recommendations (i.e. word café)

News

Joint Action

La dea Igea

Igea project
(English)

Igea:
da progetto
a sistema



RACCOLTA
Normativa e documenti
sulla gestione integrata in Italia

Next steps

Analysis of practices reported by partners

- Description of practices via semi-structured questionnaire by relevant responders
 - Quantitative
 - based on pre-defined criteria
 - Qualitative
 - why should this practice be considered a good/best practice?
 - how does this practice help in driving the change? Reasons for success (positive lessons learned) and failure (negative lessons learned)
- Drafting recommendations

SWOT analysis of National Policies

One SWOT analysis per Country/MS

- Identification of policies with Task Leaders, APs and CPs
- Identification of responders for each Country/MS

Data analysis, synthesis and final report

→ 3rd WP7 meeting, Rome July 2-3



Next Steps T1-T4

SWOT analysis of National Policies

Strengths: are internal attributes of the policy

Weaknesses: are internal attributes of the policy that need to be addressed

Opportunities are external conditions that may facilitate the policy implementation

Threats: are external conditions that may stand in the way of the policy implementation

Work on Policy Brief on National Diabetes Plans

- Involvement of WP7 Partners and respondents to the Questionnaire by second phase data collection using draft report on NDPs as a background document
- Preparation of draft Policy Brief under supervision of EU Observatory
- Debate and agreement of Policy Brief with WP7 Partners and respondents to Questionnaire ((and GB?))
- Presentation of Policy Brief during **Workshop in October** together with Workshop on “how-to-do-policy-speak “ ((GB at this point?))

The Joint Action on Chronic Diseases and Promoting Healthy Ageing across the Life Cycle (JA-CHRODIS)*



Co-funded by
the Health Programme
of the European Union

* This presentation arises from the Joint Action addressing chronic diseases and healthy ageing across the life cycle (JA-CHRODIS), which has received funding from the European Union, under the framework of the Health Programme (2008-2013).
